



## Taking care of your Sewer Network in Pittenweem – Project Update.

### Important Scottish Water Information

Address  
Address  
Address  
Address  
Postcode

We are investing in and upgrading the sewer network to help reduce sewer flooding and protect the local environment. This newsletter is to provide an update on progress as we continue the sewer improvement works and head towards the final phases of our work in East Shore.

### Update:

The works in East Shore and The New Outfall are ongoing. The new CSO chamber is installed, and the cobbled parking area is being reinstated.

### Update (continued):

The diversion works may involve some planned disruption to the water & gas supply. All customers who are affected by this will receive notification in advance with details of any planned interruption.

Work to reinstate the cobbled area around the new CSO chamber is ongoing.

### Upcoming Work – East Shore:

Work will continue in East Shore with the construction of the final two manholes and associated connection works (at No18 and No5 East Shore Approx).

This section of work will involve some changes to the traffic management in the East Shore area as the working areas move to the North side of the road. The cobbled area once reinstated will be used to manage traffic through East Shore.

### Outfall Works:

Work is continuing on the new outfall. The final section of the outfall will be constructed by utilizing a dredging vessel located within the outer harbour.

This section of work is tide dependant and working hours will vary.

### General Information:

**Traffic Management:** Localised traffic management and parking restrictions will continue to be in place in East Shore during the works. Please follow all signs in place.


**Parking:** Our site cabins have now been moved away from Mid Shore and the Mid shore car park is now fully open for parking. Our site cabins are now located in the area to the rear of Pittenweem Cemetery.



Image: Current East Shore Works

### East Shore:

The current phase of works involves carrying out localised water and gas service diversions in East Shore ahead of the final two manholes being constructed on the North side of the road.

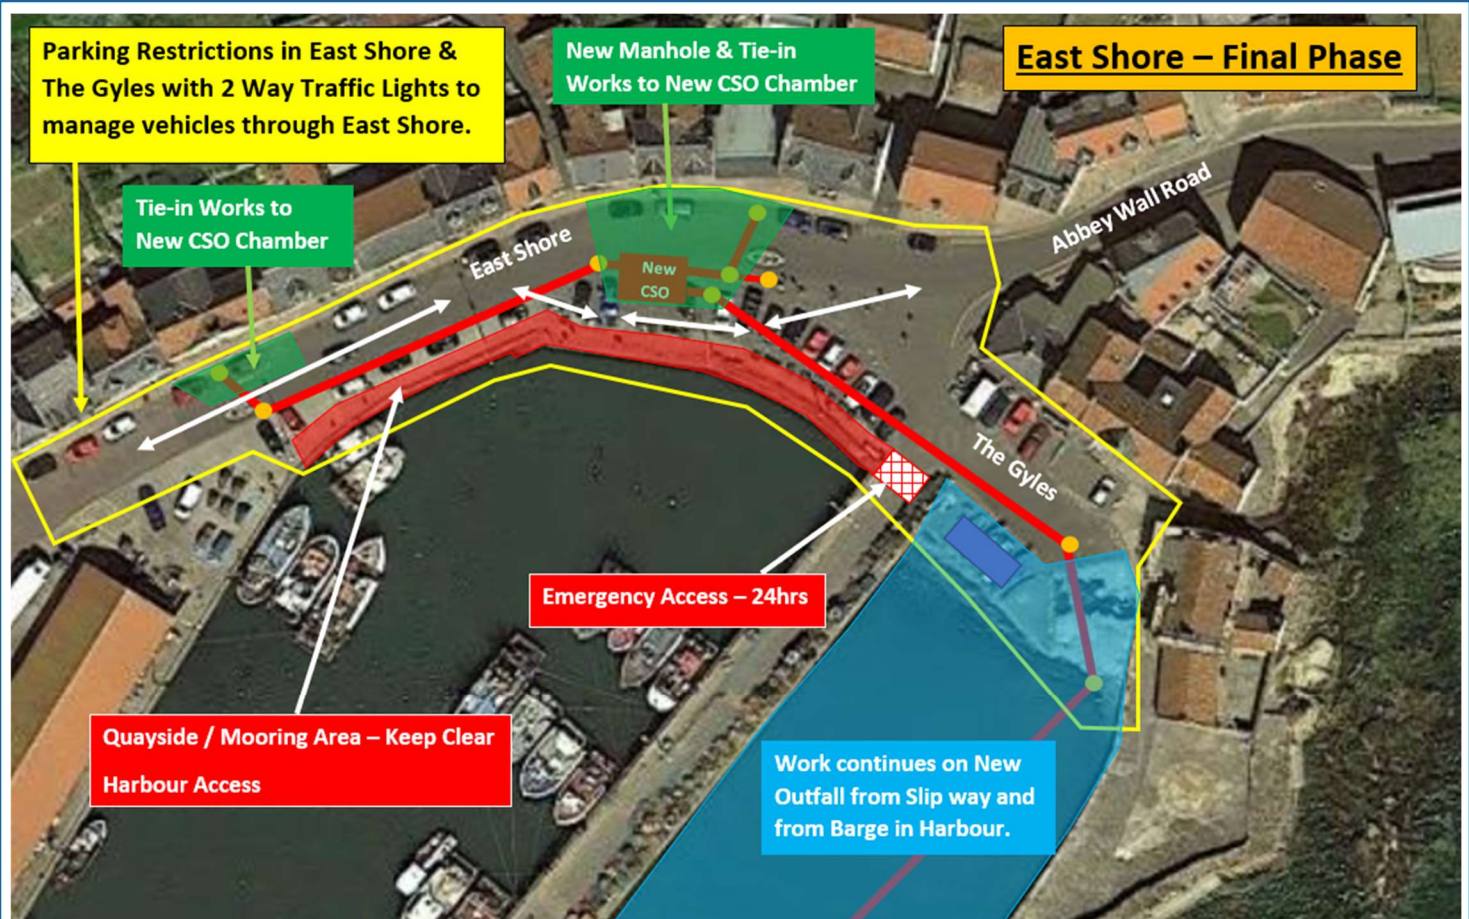

### Parking (continued):

The current traffic management is set up to ensure we maintain vehicle access through East Shore along to Mid and West Shore. Please help us to maintain this by adhering to the current parking restrictions that are in place.

As the final phases of our works are carried out, we will look to open up as much of the area as possible as the work is completed. We will however need to ensure this is done whilst maintaining a safe working area.

### Work Completion Update:

We are working hard to ensure the final stages of our works are completed as soon as possible. Our current forecast is that we hope to have works completed by mid-June.

**Project Information:** Further information about our project can be found at [www.scottishwater.co.uk/Pittenweem](http://www.scottishwater.co.uk/Pittenweem)

**We thank you for your continued patience, co-operation and understanding whilst we continue these essential works.**

**If you have any further queries, please contact Scottish Water customer helpline on 0800 0778778 quoting 'Capital/505339/CWA/Pittenweem'.**

Yours Sincerely  
*Clive Duncan*  
 Customer Manager  
 Caledonia Water Alliance

 [scottishwater.co.uk](http://scottishwater.co.uk)

 [/scottishwater](https://www.facebook.com/scottishwater)

 [@scottish\\_water](https://twitter.com/scottish_water)
